
















### Construction Status

- Construction is approximately at 38% completion
- OCS duct bank/joint trench underway
- Addressing unforeseen utility conflicts with PG&E and AT&T
- Sewer installation
  - Submittals and RFI review is ongoing
  - Potholing to identify utility conflicts with sewer alignment
  - Updated utility composite map in progress
  - Sewer trenching underway
- ADA sidewalk installation
- Temporary bus stop installation
- Traffic Control Plans Ongoing
- OCS pole foundations





# Schedule Update

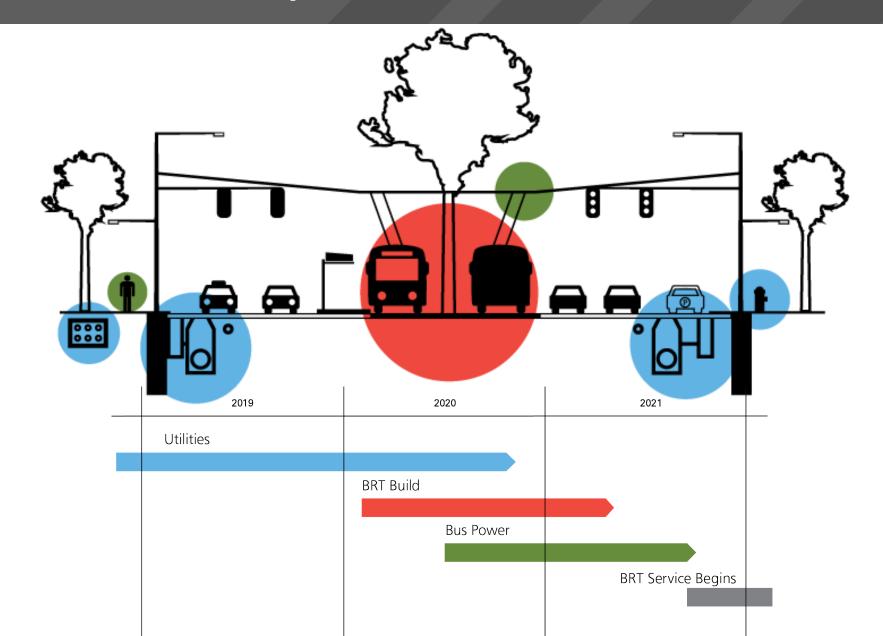

# Project Contract Modifications

### **Approved by MTA Board July 16**

- Resolved two contractor claims for unavoidable delays resulting from water and sewer issues
- Covered by project's allocated allowances, did not increase project budget
  - SFPUC provided analysis and agreed to resolution
    - Increased the contract amount by \$4.8 million
    - Increased contract duration by 279 total calendar days
      - Of claimed 279 days unavoidable delays, 135 days are justifiable due to sewer and water issues
    - Contractor agrees to drop remaining 144 delay days claims and to avoid any litigation cost for both parties

# Project Contract Modifications

### **Approved by MTA Board August 20**

- Resolved claim related to additional potholing for sewer installation necessary to address utility conflicts
- Covered by project's allocated allowances, does not increase project budget
  - SFPUC agrees to resolution
    - Increases the contract amount by \$1.7 million
    - No increase to contract duration

## Outreach

#### Ongoing outreach

- Email and text messages
  - Weekly construction forecast
  - Quarterly digital newsletter
  - Meet the Expert invites
  - Project notices
- Mailings (30k+ project neighbors)
  - Semiannual print newsletters
  - Project notices
- Monthly Public Officials' brief
- Monthly Meetings and events
  - Van Ness BAC
  - Van Ness BRT CAC
  - Meet the Expert speaker series

## Outreach

#### **Business support**

- War Memorial Opera House and San Francisco Symphony
  - Collaboration over construction and fencing in advance of Gala Week
- Color Curb Adjustments
  - New yellow zone near Daniel Burnham Court
  - New loading zone for Big Swingin' Cycles
- Car Card Campaign
  - Car cards installed on the interior of Muni buses promote visiting Van Ness businesses
  - Cards updated quarterly
  - Annual campaign value is \$76,500.00
  - Car cards are viewed by 700,000 daily riders





# Thank you



VAN NESS

IMPROVEMENT PROJECT

SFMTA.com/VanNess













